

# San Francisco Public Library Capital Projects Update

John Cunha  
Facilities Director  
and  
Lisa Valerio  
Capital Projects Manager

November 16, 2023  
San Francisco Public Library Commission





## Completed Projects:

- 750 Brannan Street Collections
- Main Library Talking Books and Braille Center (TBBC)





# 750 Brannan Street Collections



May 1, 2023: Shelf Rails Install



July 31, 2023: Floor Fill Install Start



August 14, 2023: Shelving Delivery



September 20, 2023: Shelving Installation



# Main Library Talking Books and Braille Center







## Active Projects:

- Mission Branch Library Renovation
- Chinatown Branch Library Renovation
- Ocean View Branch Library
- 190 Ninth Street Energy Efficiency



# Mission Branch Library Renovation

---



## **Scope:**

Renovation of the existing Carnegie Library

## **Current Estimate/ Budget:**

\$34M

## **Status:**

In Progress (Construction)

## **Update:**

- NTP Date: August 1, 2023
- 2% Complete: Soft demolition completed of the community room, staff workroom, and children's room





# Mission Branch Library Renovation

## Construction

---



# Chinatown Branch Library Renovation

## Scope:

Renovation of the existing Carnegie Library

## Current Estimate/ Budget:

\$37M

## Status:

95% Construction Documents Plan Development

## Update:

- Final Design
- SF Real Estate Department and the City Attorney's Office working on license agreement with neighbors





# Chinatown Branch Library Renovation

## Plan Development

---



# Ocean View Branch Library



## Goal:

~20K sf. New Library

## Budget / Estimate:

\$47M (2019 for 20K sf.)

## Allocation:

\$37.3M (through FY25)

## Status:

In Planning


## Update:

- Site Selection
- SFMTA Brotherhood/Alemany Safety Improvement Project (BASIP)
- SFCTA Brotherhood Way Safety and Circulation Plan (BWSCP)





# Site Selection - Possible Partnership

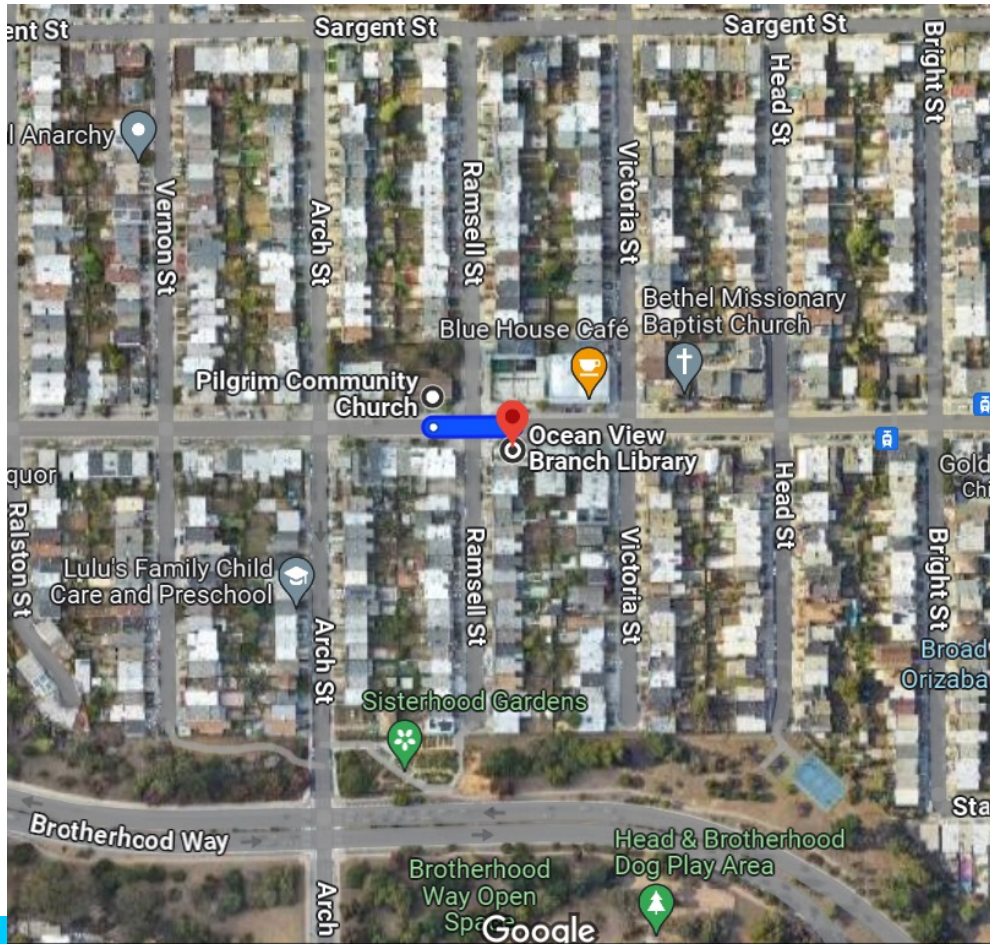

Current Ocean View Branch Library



Pilgrim Community Church / IT Bookman Center (not pictured)



# 190 Ninth Street Energy Efficiency

---

**Scope:**

Energy Efficiency-HVAC Upgrade & PV Panels

**Current Estimate/ Budget:**

\$8.9M

**Status:**

In Progress (Construction)

**Update:**

- NTP: July 17, 2023
- Mobilization expected in April 2024







## Upcoming Projects:

- Main Library:
  - Flooring
  - Roof
  - Seismic Moat
- Air Quality Improvements
- 750 Brannan Street Electric Vehicle Charging




# Main Library Projects:

## Flooring



## Roof

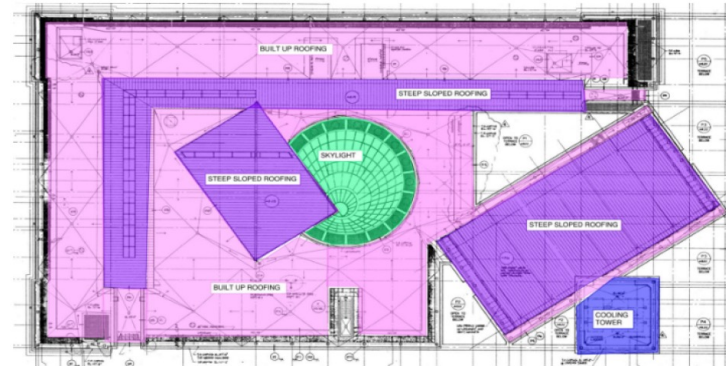

## Seismic Moat





# Air Quality Improvements & 750 Brannan Electric Vehicle Charging



# Thank You!

