

SFPL Capital Projects

John Cunha Facilities Director and Lisa Valerio Capital Projects Manager

July 18, 2024 San Francisco Library Commission



Project Updates

- Support Services Facility
- Mobile Service & High-Density Storage Facility
- Main Library
 - Roof
 - Moat
 - Safety Barriers
 - Carpet
- New Ocean View Branch Library
- Chinatown Branch Library Renovation
 - Chinatown temporary site
- Mission Branch Library Renovation




Support Services Facility: Energy Efficiency Project

- **Est. Budget:** \$8.9M
- Scope:
 - Upgrade HVAC
 - Install Photovoltaic Panel System
- Status:
 - 80% complete
 - Project completion Sept. 2024



Mobile Services & High-Density Storage Facility

- Est. Budget: \$1.6M
- Scope:
 - Install compact storage
- Status:
 - Historical Collection: partially complete
 - Periodical Collection: move to be scheduled

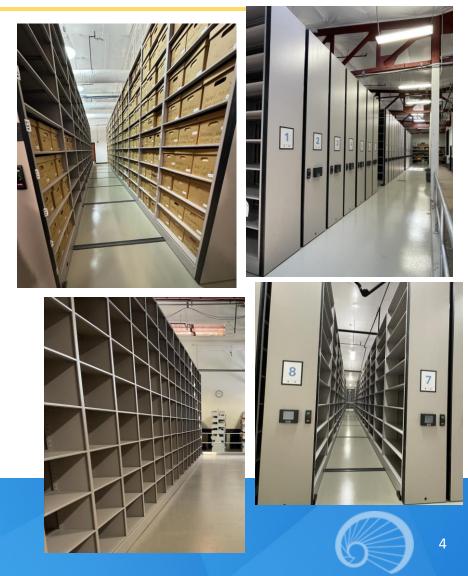

Main Library Roof & Moat



Roof

- **Est. Budget:** \$6.4M
- **Scope:** Repair roof leaks
- Schedule:
 - Tentative start July 2025




Moat

- **Est. Budget:** \$7.1M
- Scope: Replace deteriorating system
- Schedule:
 - Tentative start August 2025




Main Library: Safety Barriers & Carpet

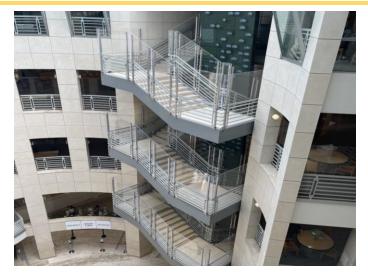

Safety Barriers

- Est. Budget: \$4M
- Scope: Enhance safety
- Schedule:
 - Est. start Jan. 2025

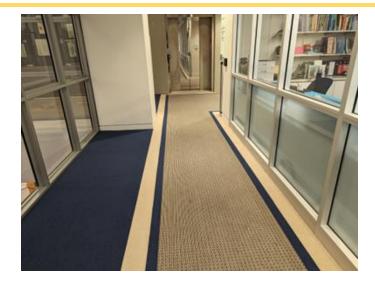

Carpet

- Est. Budget: TBD
- Scope: Replace worn carpet
- Schedule:
 - TBD



Ocean View Branch Library

Goal: New Ocean View Branch Library

Site Evaluation

- Orizaba
 - 20,000 SF
 - \$65M-\$94M Updated Cost Estimate Range*

Site selection to align with

- Planning Department Report
- Community feedback

Exploring joint-use partnership


• Pilgrim Community Church/IT Bookman Center



*7.10.24-Public Works consultant cost estimate



NEW Ocean View Branch Library: Orizaba Site – Preliminary Timeline

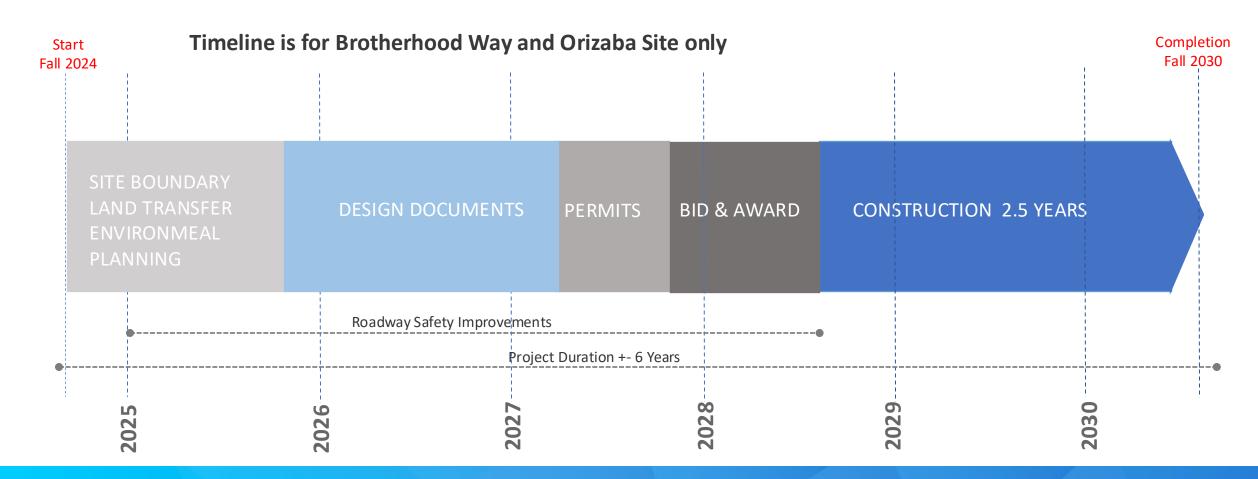



Ocean View Branch Library: Community Meetings

• Three meetings in May 2024:

- Provided project background & overview
- Reviewed standard branch library services
- Collected community design goals

• Community Feedback:

- A library that reflects the community
- Safe access
- No consensus on Brotherhood Way location
- Flexible space to meet evolving needs
- Access to social services, resources, and enrichment classes







Chinatown Branch Library Renovation

- Est. Budget: \$37M
- Completed:
 - Historic Preservation Commission
 - Environmental & Planning Entitlements
 - Department of Building Inspection Site Permit



• Schedule:


- Est. Construction Feb. 2025
- Project completion Spring 2027





Chinatown Renovation Temporary Library


- Location:
 - 950 Grant Street, a few blocks from Him Mark Lai Chinatown Library
- Specifications:
 - 4,200 square feet
 - Main floor: public space
 - Mezzanine: staff space
- Status:
 - Board of Supervisor lease approval in late summer or early fall 2024
 - Library tentative move in December 2024 or January 2025

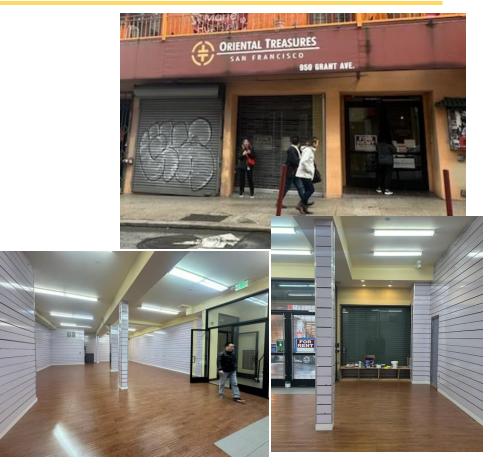




Mission Branch Library Renovation

- Est. Budget: \$34M
- Schedule:
 - Construction started-Aug. 2023
 - Est. Project completion- Jan. 2026
- Project impacts:
 - Required additional shoring and under pinning
 - Structural revisions

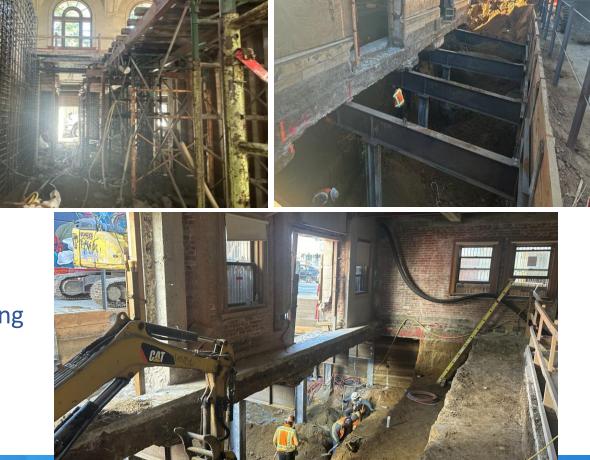



Mission Branch Library Renovation

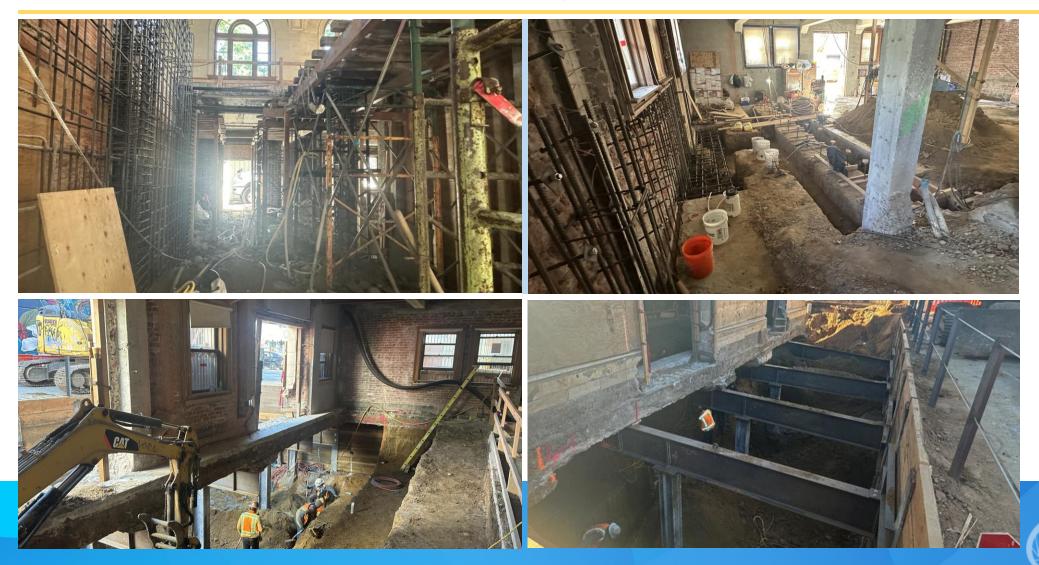



Thank you.

